


1/9/2007

Overall:

- BellSouth has delivered 9 of the 10 outstanding local loops
- SU working on installing UPS and P5
- Sun America IRU signed
- Southern Ring is 75% complete

Issues:

- ITC^DeltaCom collocation contract
- McLeodUSA collocation contract
- Level3 collocation contract
- AT&T IRU
- Missing local loop dark fiber routes

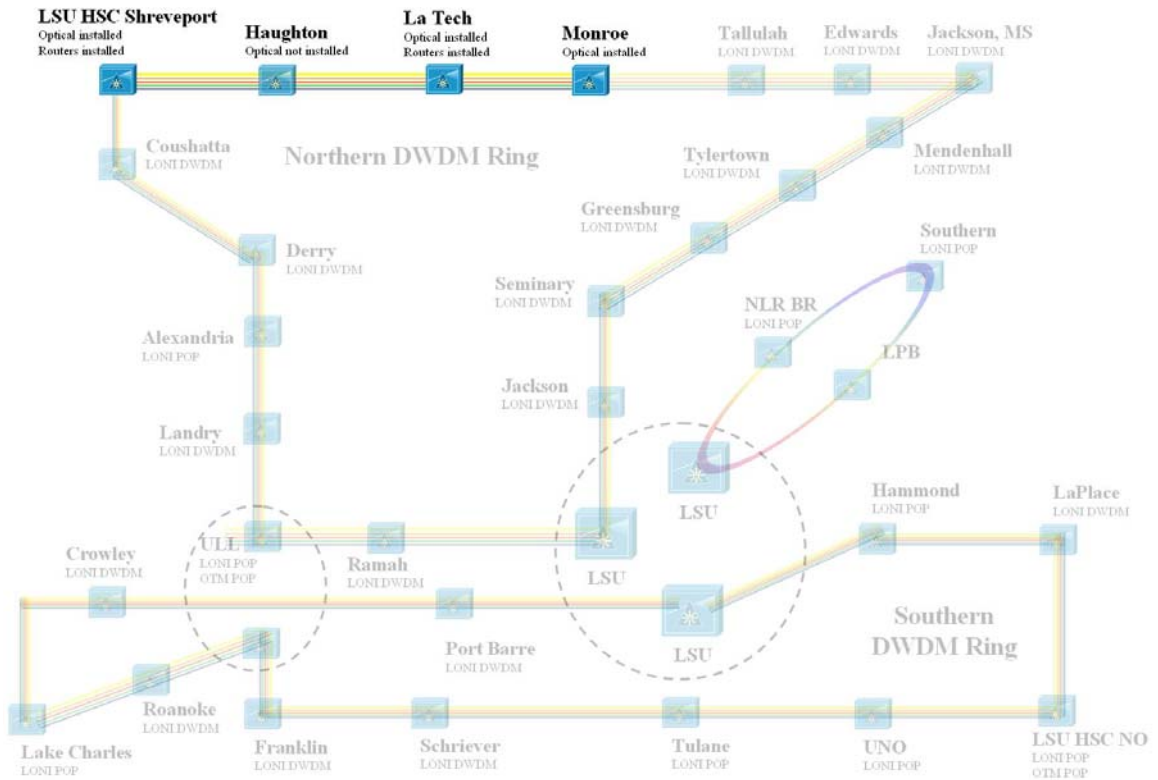


1/9/2007

Shreveport to Monroe:
Completed

Pending

- Fiber Characterization
- BellSouth Local Loop from LSU HSC to Sun America
- McLeodUSA collocation contract
- McLeodUSA Haughton Optical Installation

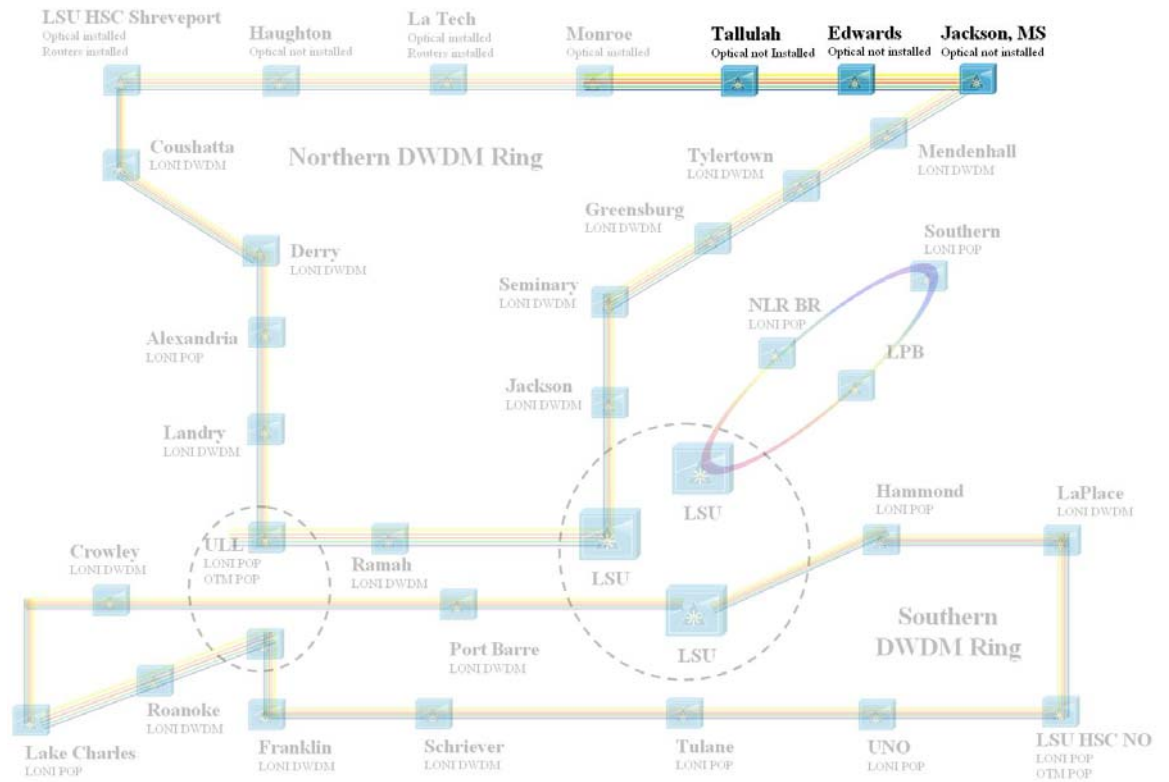

1/9/2007


Monroe to Jackson, MS:
Completed

Pending

ITC^DeltaCom collocation contract
Tallulah Optical Installation
Jackson, MS Optical Installation

Missing

Dark Fiber local loop

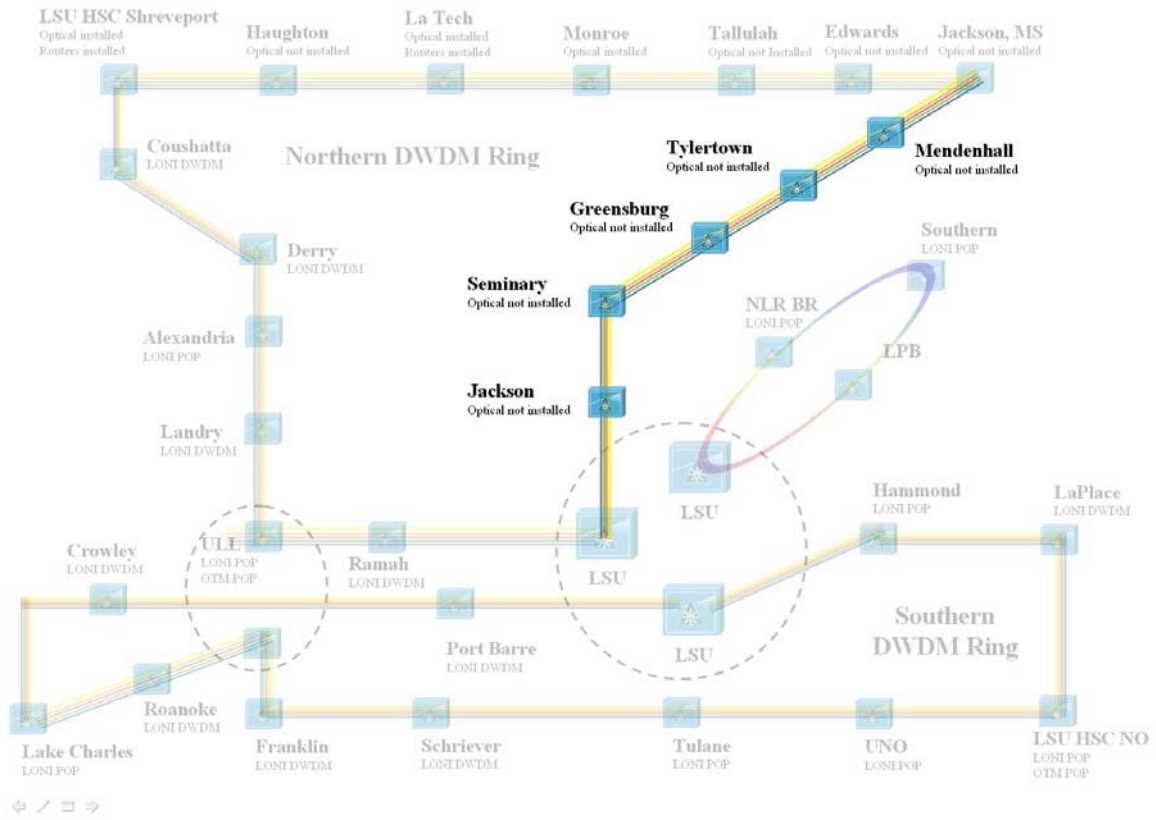


1/9/2007

Jackson, MS to Baton Rouge:
Completed

Pending

- Level3 collocation contract
- Site Survey of the Route
- Fiber Characterization
- Mendenhall, MS Optical Installation
- Tylectown, MS Optical Installation
- Greensburg, MS Optical Installation
- Seminary, MS Optical Installation
- Jackson, LA Optical Installation
- L Band DCUs from Cisco/BellSouth

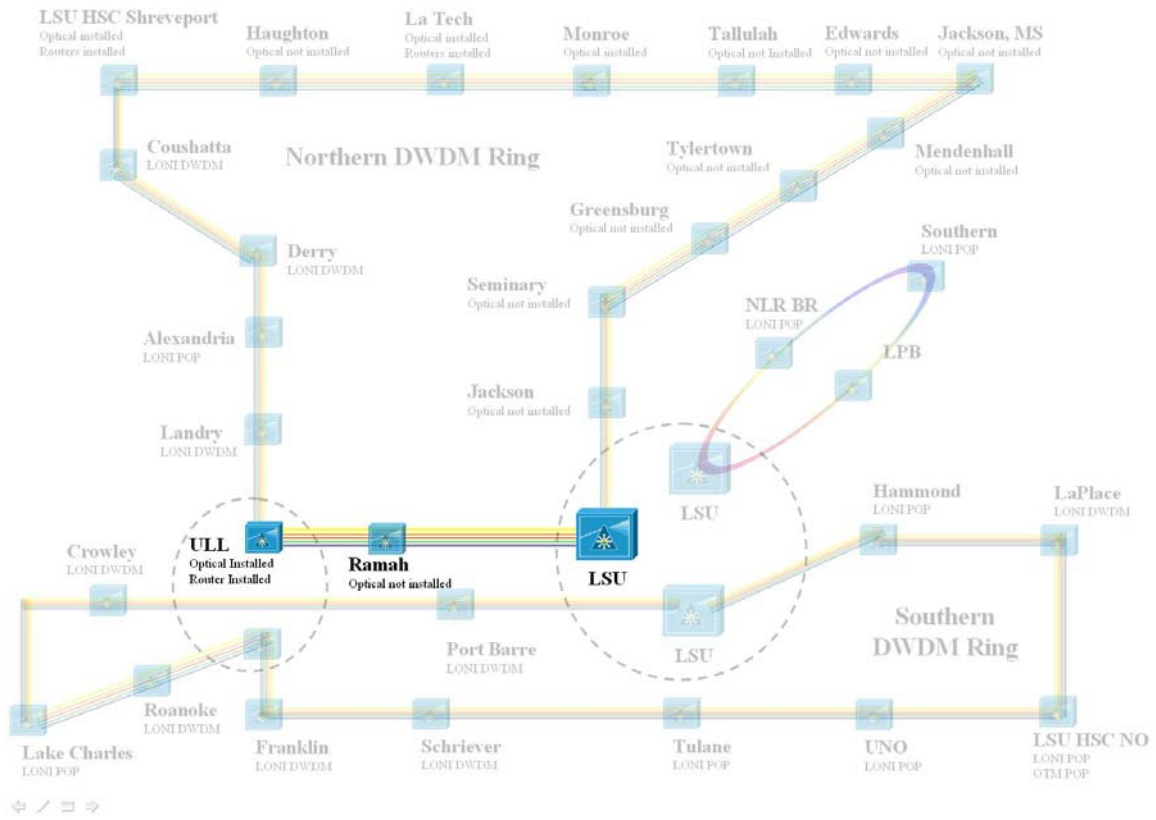

1/9/2007


Baton Rouge to Lafayette:
Completed

Pending

Working with ULL to schedule service turn-up
Waiting on LITE to fix either fiber and/or equipment problems

Missing

Dark Fiber local loop in Lafayette

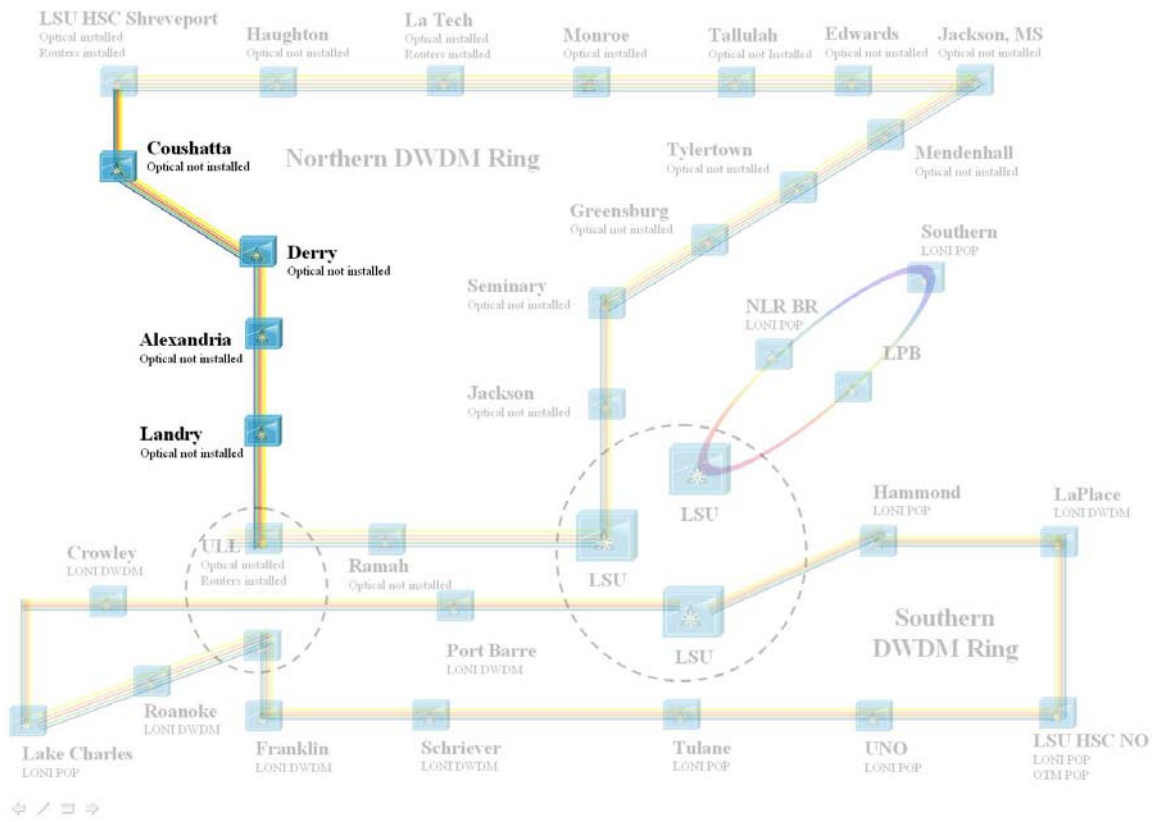


1/9/2007

Lafayette to Shreveport:
Completed

Pending

- Anticipating equipment installations starting the week of 1/15/07.
- Fiber Characterization
- St. Landry Optical Installation
- Alexandria Optical Installation
- Derry Optical Installation
- Coshatta Optical Installation
- BellSouth Local Loop from HSC to Sun America

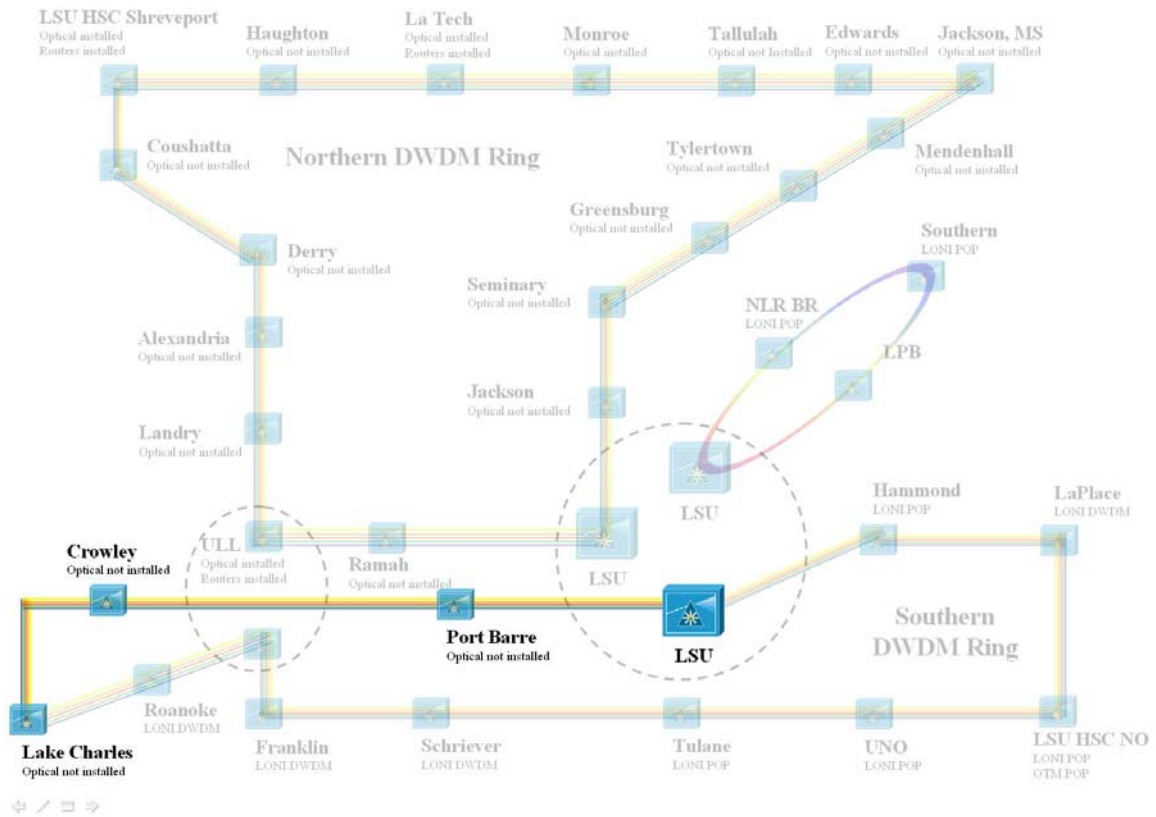

1/9/2007


Lake Charles to Baton Rouge:
Completed

Pending

- AT&T IRU
- Route Construction by AT&T
- Site Survey of the Route
- Fiber Assignments
- Fiber Characterization
- Lake Charles Optical and Routers Installation
- Crowley Optical Installation
- Port Barre Optical Installation
- Cisco Equipment Order for LPB

Missing

- Dark Fiber local loop

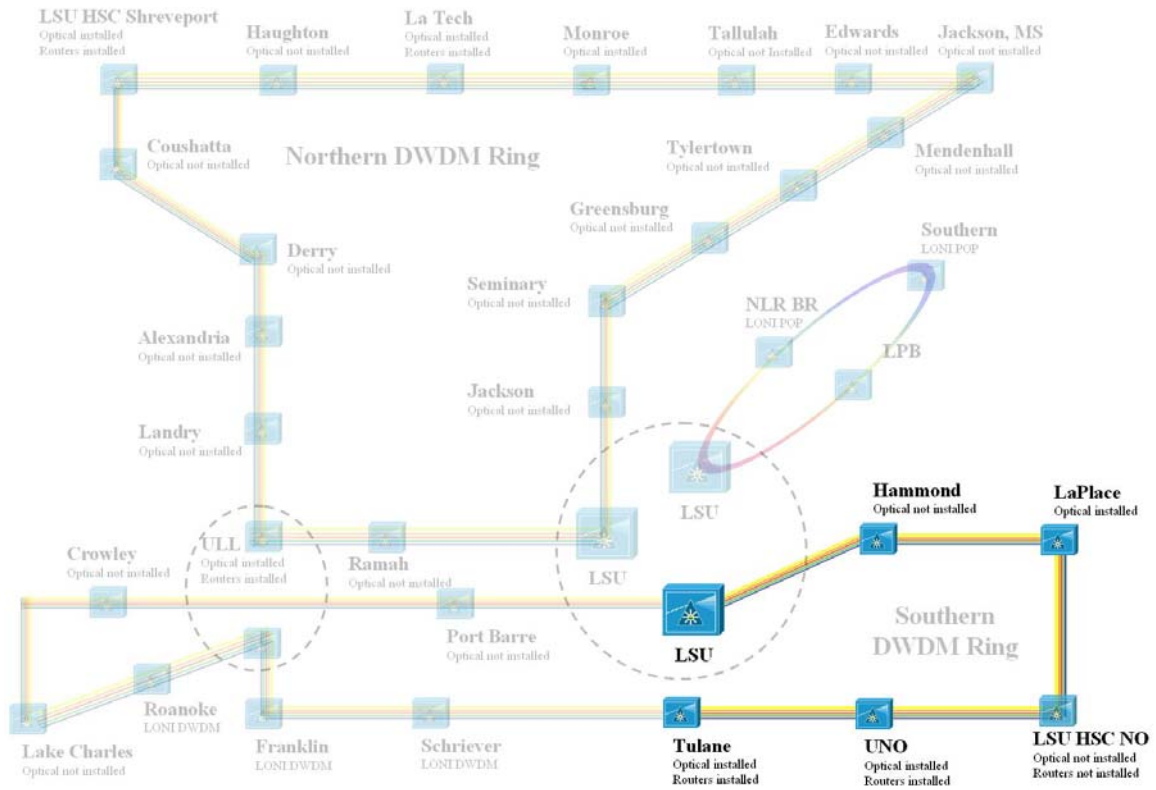


1/9/2007

Baton Rouge to New Orleans:
Completed

Pending

Working a fiber issue between LSU and Hammond
Working a equipment issue at UNO

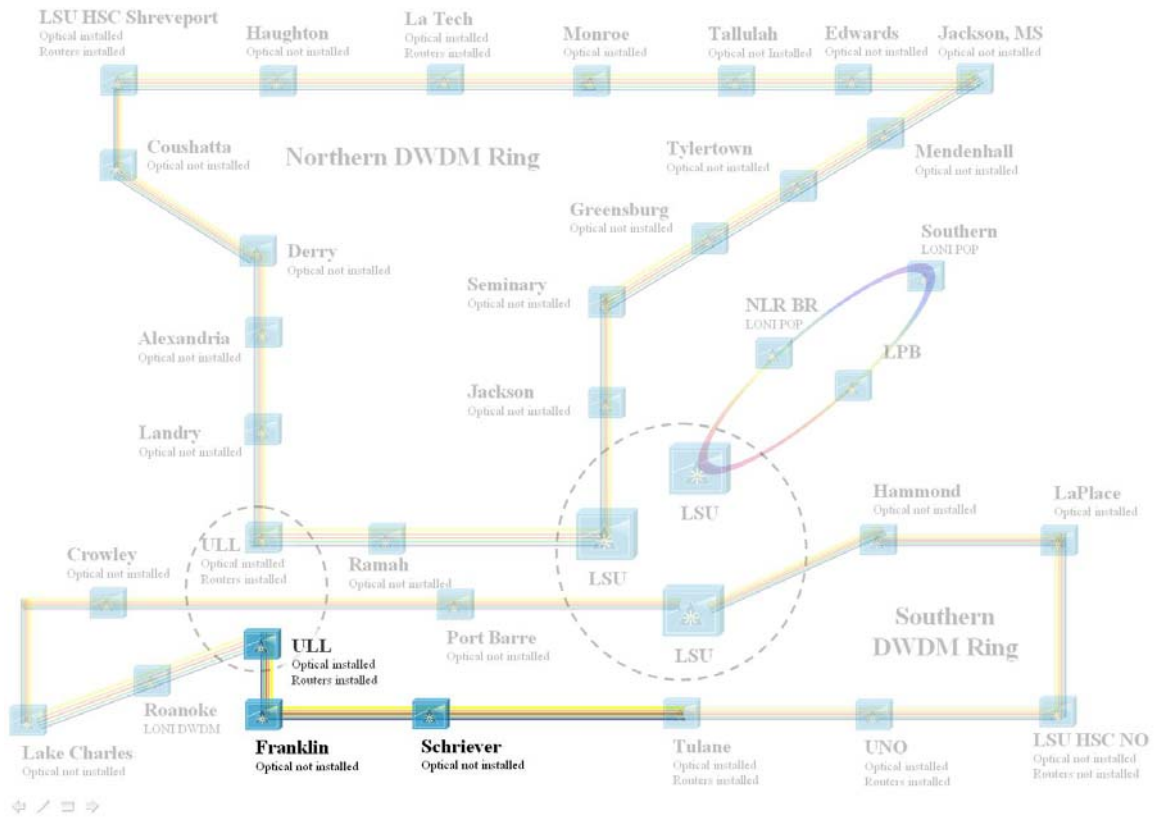

1/9/2007


New Orleans to Lafayette:
Completed

Pending

Working a fiber performance issue with BellSouth between Tulane and Qwest PoP in New Orleans

Potential New Costs

Build our own fiber cable between Tulane (1555 Poydras) and Qwest (1340 Poydras)

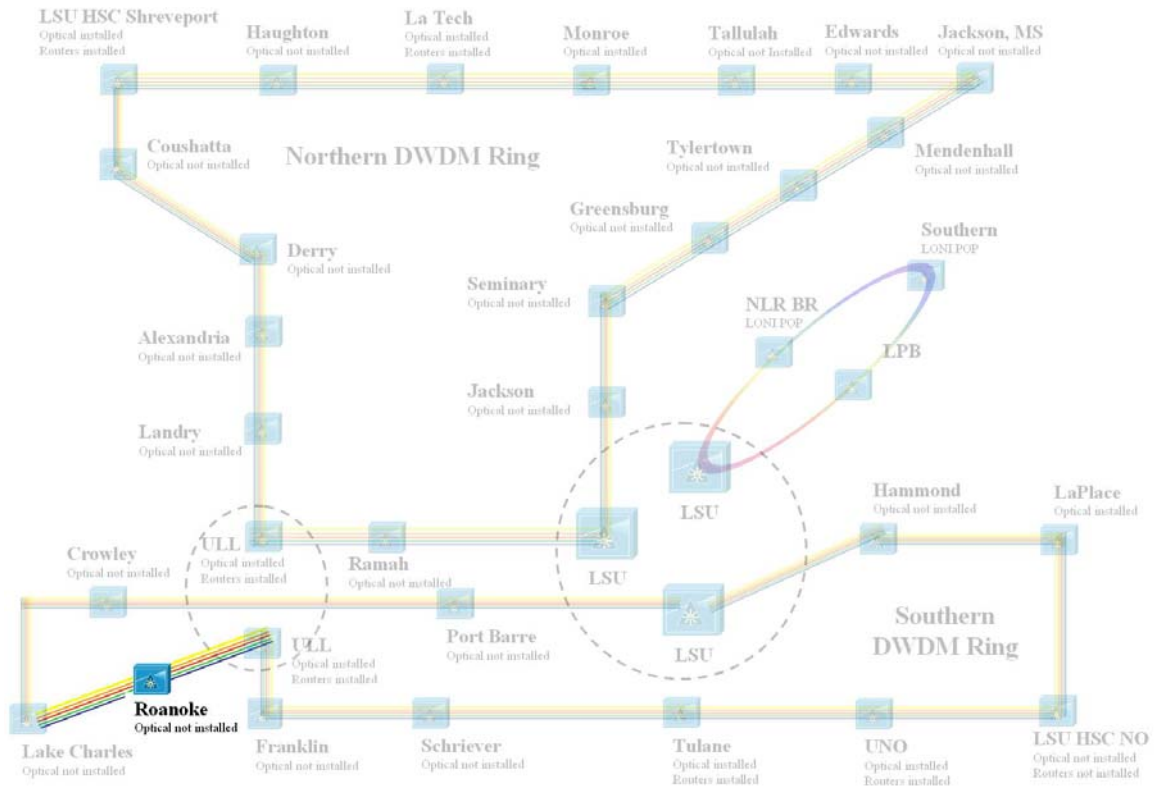


1/9/2007

Lafayette to Lake Charles:
Completed

Pending

- Site Survey of the Route
- Fiber Characterization
- Cisco Equipment Order for LPB
- Roanoke Optical Installation

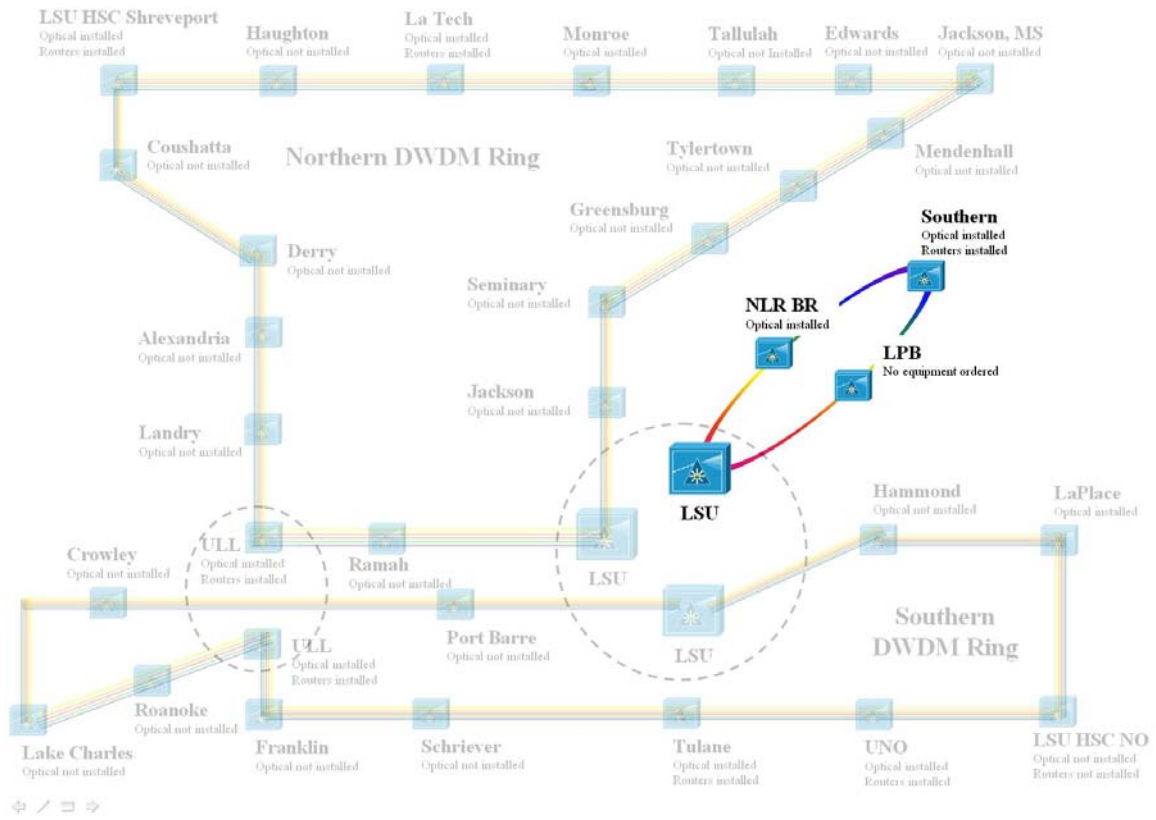

1/9/2007

Baton Rouge Ring:
Completed

Everything is production except for LPB equipment

Pending

SU UPS Installation estimated late February
 SU P5 Installation estimated for March
 Cisco Equipment Order for LPB
